










ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, 'M
1		UCHSC PA Student Assessment Tool	63.63 days	Wed 1/21/04	Tue 3/23/04			
2	✓	Team Agreement	7 days	Wed 1/21/04	Tue 1/27/04			
3	✓	Draft Team Agreement	2 days	Wed 1/21/04	Thu 1/22/04		Lisa Foegen	
4	✓	Review Team Agreement	2 days	Fri 1/23/04	Sat 1/24/04	3	Jim Ladd[25%],Dianne Calhoun[25%],Brian	
5	✓	Revise Team Agreement	1 day	Mon 1/26/04	Mon 1/26/04	3,4	Jim Ladd[50%],Lisa Foegen[50%]	
6	✓	Sign Team Agreement and Submit	1 day	Tue 1/27/04	Tue 1/27/04	3,4,5	Lisa Foegen[20%],Dianne Calhoun[20%],J	
7	✓	Scope	4 days	Wed 1/28/04	Sat 1/31/04			
8	✓	Determine project scope	2 days	Wed 1/28/04	Thu 1/29/04	3,4,5,6	Lisa Foegen[20%],Jim Ladd[20%],Dianne (
9	✓	Define preliminary resources	2 days	Fri 1/30/04	Sat 1/31/04	8	Jim Ladd[50%],Lisa Foegen[50%]	
10	✓	Draft Design Analysis	7 days	Wed 1/28/04	Tue 2/3/04		Dianne Calhoun[50%],Brian Knowles, \	
11	✓	Draft Design Analysis	2 days	Wed 1/28/04	Thu 1/29/04		Brian	
12	✓	Review Draft Design Analysis	2 days	Fri 1/30/04	Sat 1/31/04	11	Lisa Foegen[20%],Jim Ladd[20%],Dianne (
13	✓	Revise Draft Design Analysis	2 days	Sun 2/1/04	Mon 2/2/04	12	Brian Knowles	
14	✓	Final Draft Design Analysis	1 day	Tue 2/3/04	Tue 2/3/04	13	Brian Knowles	
15	✓	Draft Project Definition	7 days	Wed 1/28/04	Tue 2/3/04			
16	✓	Draft Project Definition	2 days	Wed 1/28/04	Thu 1/29/04		Jim Ladd	
17	✓	Review Draft Project Definition	2 days	Fri 1/30/04	Sat 1/31/04	16	Lisa Foegen	
18	✓	Revise Draft Project Definition	2 days	Sun 2/1/04	Mon 2/2/04	17	Jim Ladd	
19	✓	Final Draft Project Definition	1 day	Tue 2/3/04	Tue 2/3/04	18	Jim Ladd	
20	✓	Final Design Analysis	7 days	Wed 2/4/04	Tue 2/10/04	14	Brian Knowles,Dianne Calhoun[50%], \	
21	✓	Final Design Analysis	3 days	Wed 2/4/04	Fri 2/6/04		Brian	
22	✓	Review Final Design Analysis	1 day	Sat 2/7/04	Sat 2/7/04	21	Lisa Foegen[20%],Jim Ladd[20%],Dianne (
23	✓	Revise Final Design Analysis	2 days	Sun 2/8/04	Mon 2/9/04	22	Brian Knowles	
24	✓	Final Design Analysis	1 day	Tue 2/10/04	Tue 2/10/04	23	Brian Knowles	
25	✓	Final Project Definition	7 days	Wed 2/4/04	Tue 2/10/04	19		
26	✓	Final Project Definition	3 days	Wed 2/4/04	Fri 2/6/04		Jim Ladd	
27	✓	Review Final Project Definition	1 day	Sat 2/7/04	Sat 2/7/04	26	Lisa Foegen	
28	✓	Revise Final Project Definition	2 days	Sun 2/8/04	Mon 2/9/04	27	Jim Ladd	
29	✓	Final Project Definition	1 day	Tue 2/10/04	Tue 2/10/04	28	Jim Ladd	
30	✓	Client Approval	2 days	Mon 2/9/04	Tue 2/10/04		Anita Glicken	
31	✓	Client Approval	2 days	Mon 2/9/04	Tue 2/10/04		Anita Glicken	
32	✓	Client Evaluation	2 days	Mon 2/9/04	Tue 2/10/04		Anita Glicken	

Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Page 1





















ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, 'M
33		Client Evaluation	2 days	Mon 2/9/04	Tue 2/10/04		Anita Glicken	
34								
35		High-level Design Blueprint	14 days	Wed 2/11/04	Tue 2/24/04		All	
36		Structure Content	5 days	Wed 2/11/04	Sun 2/15/04		All	
37		Present Learning Strategy	5 days	Wed 2/11/04	Sun 2/15/04		All	
38		Plan for Reviews	3 days	Fri 2/13/04	Sun 2/15/04		All	
39		Plan for Technical Tests	3 days	Fri 2/13/04	Sun 2/15/04		DC - Support,JL - Support	
40		Submit Draft High-level Design Blueprint to class	1 hr	Tue 2/17/04	Tue 2/17/04	36,37,38,39	All	
41		Submit Draft High-level Design Blueprint for client review	1 hr	Tue 2/17/04	Tue 2/17/04	36,37,38,39	JL - Support	
42		Client Review	3 days	Tue 2/17/04	Fri 2/20/04	41	AG - Client	
43		Respond to review comments	3 days	Fri 2/20/04	Mon 2/23/04	42	LF - Support,JL - Support	
44		Submit Final High-level Design Blueprint for client approv:	1 hr	Mon 2/23/04	Mon 2/23/04	43	LF - Support	
45		Client Approval	1 day	Mon 2/23/04	Tue 2/24/04	44	AG - Client	
46		Submit Final High-level Design Blueprint	1 hr	Tue 2/24/04	Tue 2/24/04	45	JL - Support	
47		High-level Design Blueprint complete	0 days	Tue 2/24/04	Tue 2/24/04	46		
48								
49		Detailed Design Blueprint	28 days	Wed 2/25/04	Tue 3/23/04	35	All	
50		Develop a prototype	13 days	Wed 2/25/04	Tue 3/9/04		All	
51		Develop storyboards	2 days	Wed 2/25/04	Thu 2/26/04			
52		Design graphic user interface	3 days	Fri 2/27/04	Sun 2/29/04	51	VE - Lead	
53		Review client requests	1.5 hrs	Fri 2/27/04	Fri 2/27/04		VE - Lead	
54		Develop specifications	1.5 hrs	Fri 2/27/04	Fri 2/27/04	53	VE - Lead	
55		Develop a template	1 day	Fri 2/27/04	Fri 2/27/04		VE - Lead	
56		Color palette	1 day	Fri 2/27/04	Fri 2/27/04			
57		Content placeholders	1 day	Fri 2/27/04	Fri 2/27/04			
58		Navigation	1 day	Fri 2/27/04	Fri 2/27/04			
59		Action buttons	1 day	Fri 2/27/04	Fri 2/27/04			
60		Create Forms from template	2 days	Sat 2/28/04	Sun 2/29/04	55		
61		Graphic user interface complete	0 days	Sun 2/29/04	Sun 2/29/04	60		
62		Design databse	7.75 days	Wed 2/25/04	Wed 3/3/04		DC - Lead,BK - Support,JL - Support	
63		Review client requests	1 hr	Wed 2/25/04	Wed 2/25/04		DC - Lead	
64		Develop specifications	1 hr	Wed 2/25/04	Wed 2/25/04	63	DC - Lead	


Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, 'M
65		Identify fields	4 hrs	Thu 2/26/04	Thu 2/26/04	63,64		
66		Identify key and primary fields	2 hrs	Thu 2/26/04	Thu 2/26/04	65		
67		Design tables	3 days	Thu 2/26/04	Sun 2/29/04	66		
68		Flowchart relationships among tables	1 day	Sun 2/29/04	Mon 3/1/04	67		
69		Create tables in MS Access	2 days	Mon 3/1/04	Wed 3/3/04	68		
70		Database complete	0 days	Wed 3/3/04	Wed 3/3/04	69		
71		Connect graphic user interface and database	3 days	Wed 3/3/04	Sat 3/6/04	62	DC - Lead,BK - Support,JL - Support	
72		Review client requests	1 hr	Wed 3/3/04	Wed 3/3/04			
73		Develop specifications	1 hr	Wed 3/3/04	Wed 3/3/04	72		
74		Flowchart the process	2 hrs	Thu 3/4/04	Thu 3/4/04	72,73		
75		Describe ColdFusion tags required	4 hrs	Thu 3/4/04	Thu 3/4/04	74		
76		Write ColdFusion code to connect interface wii	2 days	Thu 3/4/04	Sat 3/6/04	75		
77		Design report functionality	2 days	Sat 3/6/04	Mon 3/8/04	71	DC - Lead,LF - Support,BK - Support	
78		Review client requests	1 hr	Sat 3/6/04	Sat 3/6/04			
79		Develop specifications	1 hr	Sat 3/6/04	Sat 3/6/04	78		
80		Identify reports to be run	2 hrs	Sun 3/7/04	Sun 3/7/04	78,79		
81		Flowchart information to and from database	2 hrs	Sun 3/7/04	Sun 3/7/04	80		
82		Describe ColdFusion tags required	1 day	Sun 3/7/04	Mon 3/8/04	81		
83		Write ColdFusion code to run reports	2 days	Sat 3/6/04	Mon 3/8/04			
84		Prototype complete	0 days	Mon 3/8/04	Mon 3/8/04	83		
85		Document publishing guidelines	12 days	Wed 2/25/04	Sun 3/7/04		LF - Lead,JL - Support	
86		Set style guidelines	12 days	Wed 2/25/04	Sun 3/7/04			
87		Set technical standard for authoring	12 days	Wed 2/25/04	Sun 3/7/04			
88		Set the minimum configuration for viewing	12 days	Wed 2/25/04	Sun 3/7/04			
89		Develop templates	12 days	Wed 2/25/04	Sun 3/7/04			
90		Establish production specifications	12 days	Wed 2/25/04	Sun 3/7/04			
91		Publishing guidelines complete	0 days	Sun 3/7/04	Sun 3/7/04	86,87,88,89,90		
92		Submit Draft Detailed Design Blueprint	0 hrs	Tue 3/9/04	Tue 3/9/04	91,84		
93		Usability test for prototype	8 days	Sat 3/6/04	Sat 3/13/04		VE - Lead,LF - Support,BK - Support	
94		Develop functional test plans using product specific	1 day	Sat 3/6/04	Sat 3/6/04		VE - Lead	
95		Develop integration test plans using product specific	1 day	Sat 3/6/04	Sat 3/6/04		VE - Lead	
96		Functional Testing	5 days	Tue 3/9/04	Sat 3/13/04	84		


Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Page 3

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	8, 'M
97		Test prototype functionality	4 hrs	Tue 3/9/04	Tue 3/9/04			
98		Identify anomolies to prototype	4 hrs	Tue 3/9/04	Tue 3/9/04	97		
99		Modify code to solve anomolies	3 days	Wed 3/10/04	Fri 3/12/04	98		
100		Re-test modified code	1 day	Sat 3/13/04	Sat 3/13/04	99		
101		Functional testing complete	0 days	Sat 3/13/04	Sat 3/13/04	100		
102		Integration Testing	5 days	Tue 3/9/04	Sat 3/13/04	84		
103		Test prototype integration	4 hrs	Tue 3/9/04	Tue 3/9/04			
104		Identify anomolies to prototype	4 hrs	Tue 3/9/04	Tue 3/9/04	103		
105		Modify code to solve anomolies	3 days	Wed 3/10/04	Fri 3/12/04	104		
106		Re-test modified code	1 day	Sat 3/13/04	Sat 3/13/04	105		
107		Integration testing complete	0 days	Sat 3/13/04	Sat 3/13/04	106		
108		Usability testing complete	0 days	Sat 3/13/04	Sat 3/13/04	101,107		
109		SME and Sponsor reviews	11 days	Fri 3/12/04	Mon 3/22/04	84	JL Lead,LF - Support	
110		Plan Formal Technical Review	3 days	Fri 3/12/04	Sun 3/14/04			
111		Send review to Anita and Monica w/ cover letter	1 hr	Mon 3/15/04	Mon 3/15/04	110		
112		Anita and Monica complete review	5 days	Mon 3/15/04	Sat 3/20/04	111	AG - Client,MY - IT Client	
113		Respond to reviewers' comments	2 days	Sun 3/21/04	Mon 3/22/04	112		
114		Submit Final Detailed Design Blueprint for client approval	1 hr	Mon 3/22/04	Mon 3/22/04		LF - Lead	
115		Client Approval	1 day	Mon 3/22/04	Tue 3/23/04	114	AG - Client	
116		Submit Final Detailed Design Blueprint	1 hr	Tue 3/23/04	Tue 3/23/04	115	JL Lead	
117		Detailed Design Blueprint complete	0 days	Tue 3/23/04	Tue 3/23/04	116		





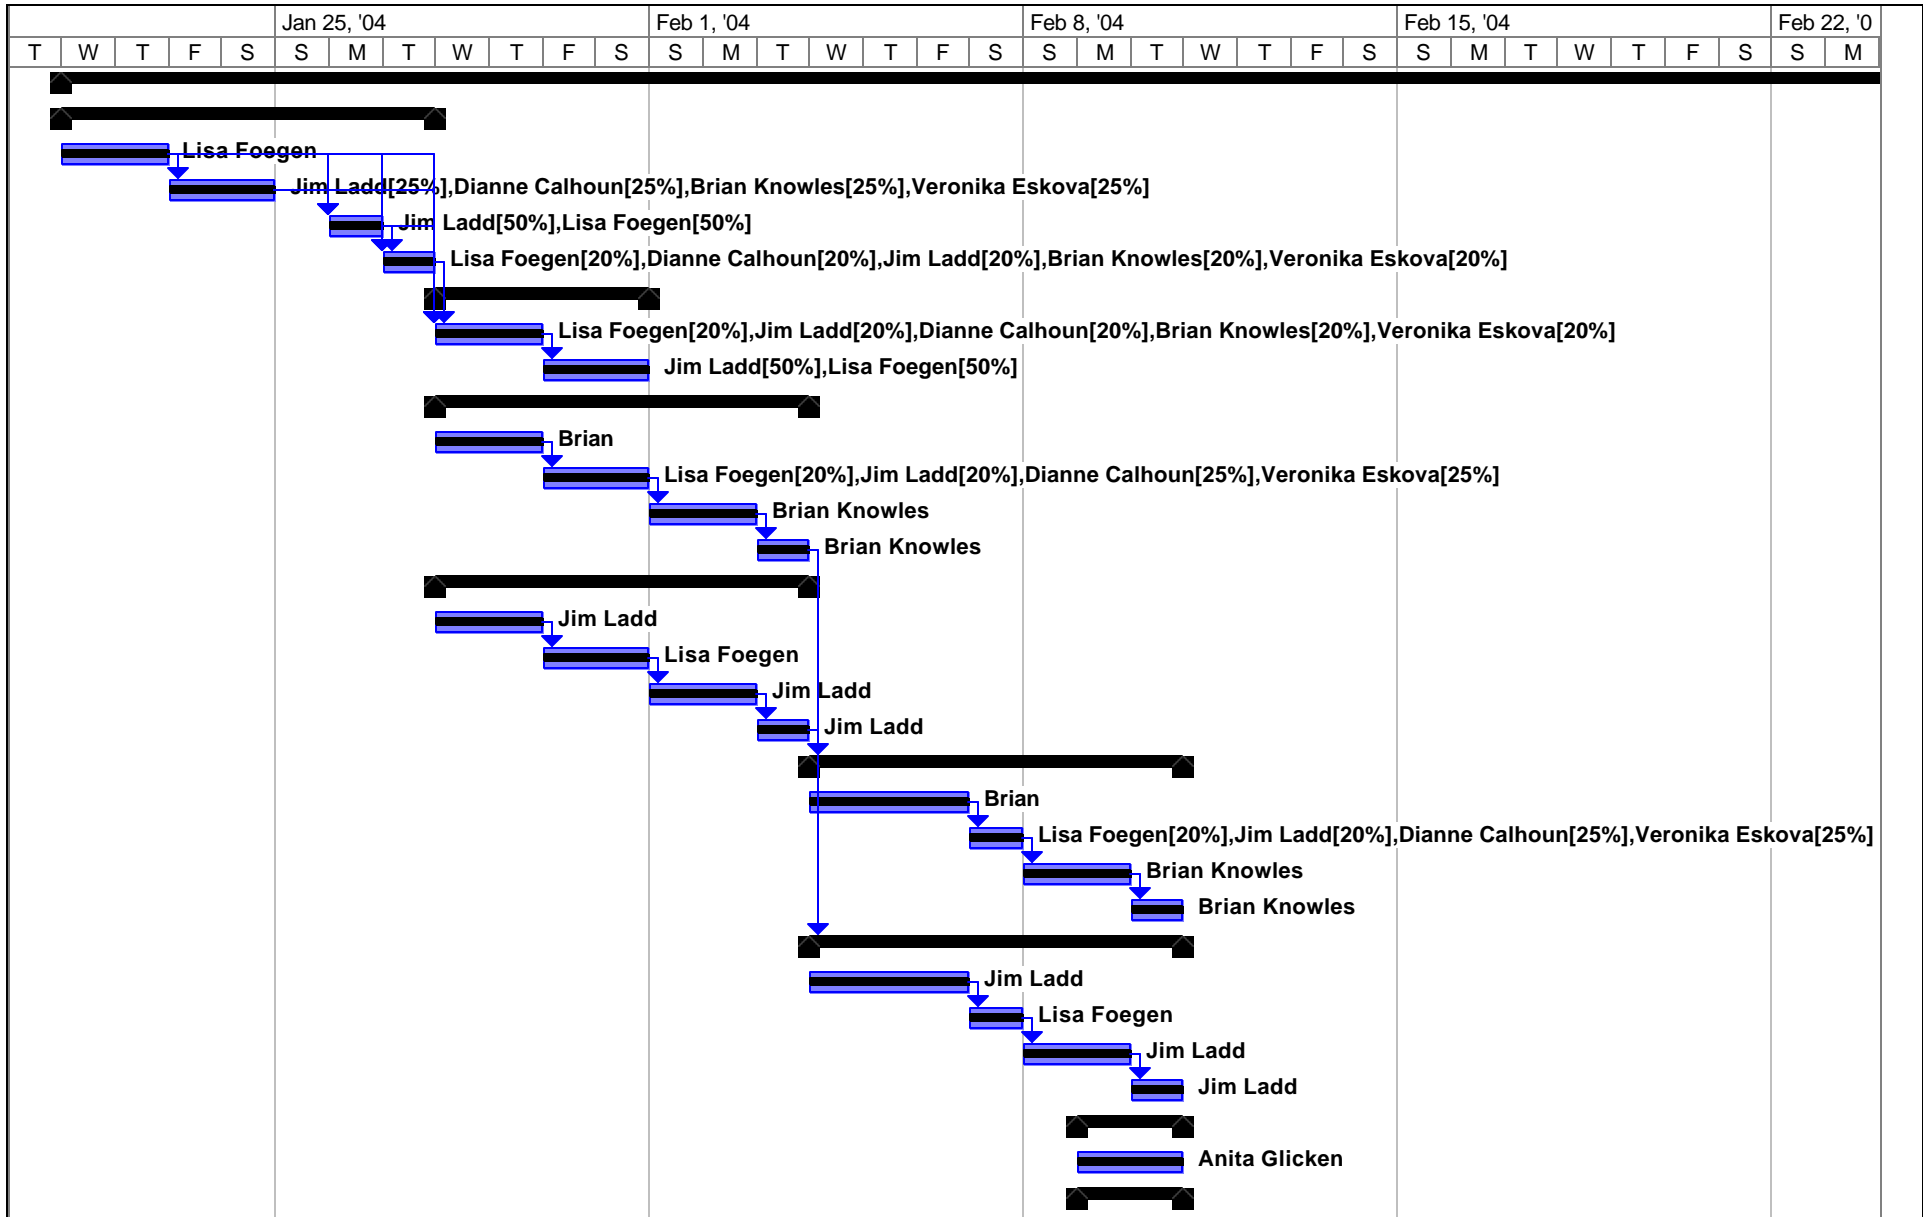






Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: PASAT Project Plan_v3
 Date: Wed 6/16/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	










					Jan 25, '04					Feb 1, '04					Feb 8, '04					Feb 15, '04					Feb 22, '0									
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










					Jan 25, '04					Feb 1, '04					Feb 8, '04					Feb 15, '04					Feb 22, '0									
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M


Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

					Feb 29, '04					Mar 7, '04					Mar 14, '04					Mar 21, '04					Mar 28, '0		
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
<div data-bbox="100 906 226 933" data-label="Text"> <p>skova[25%]</p> </div>																											

Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: PASAT Project Plan_v3 Date: Wed 6/16/04	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

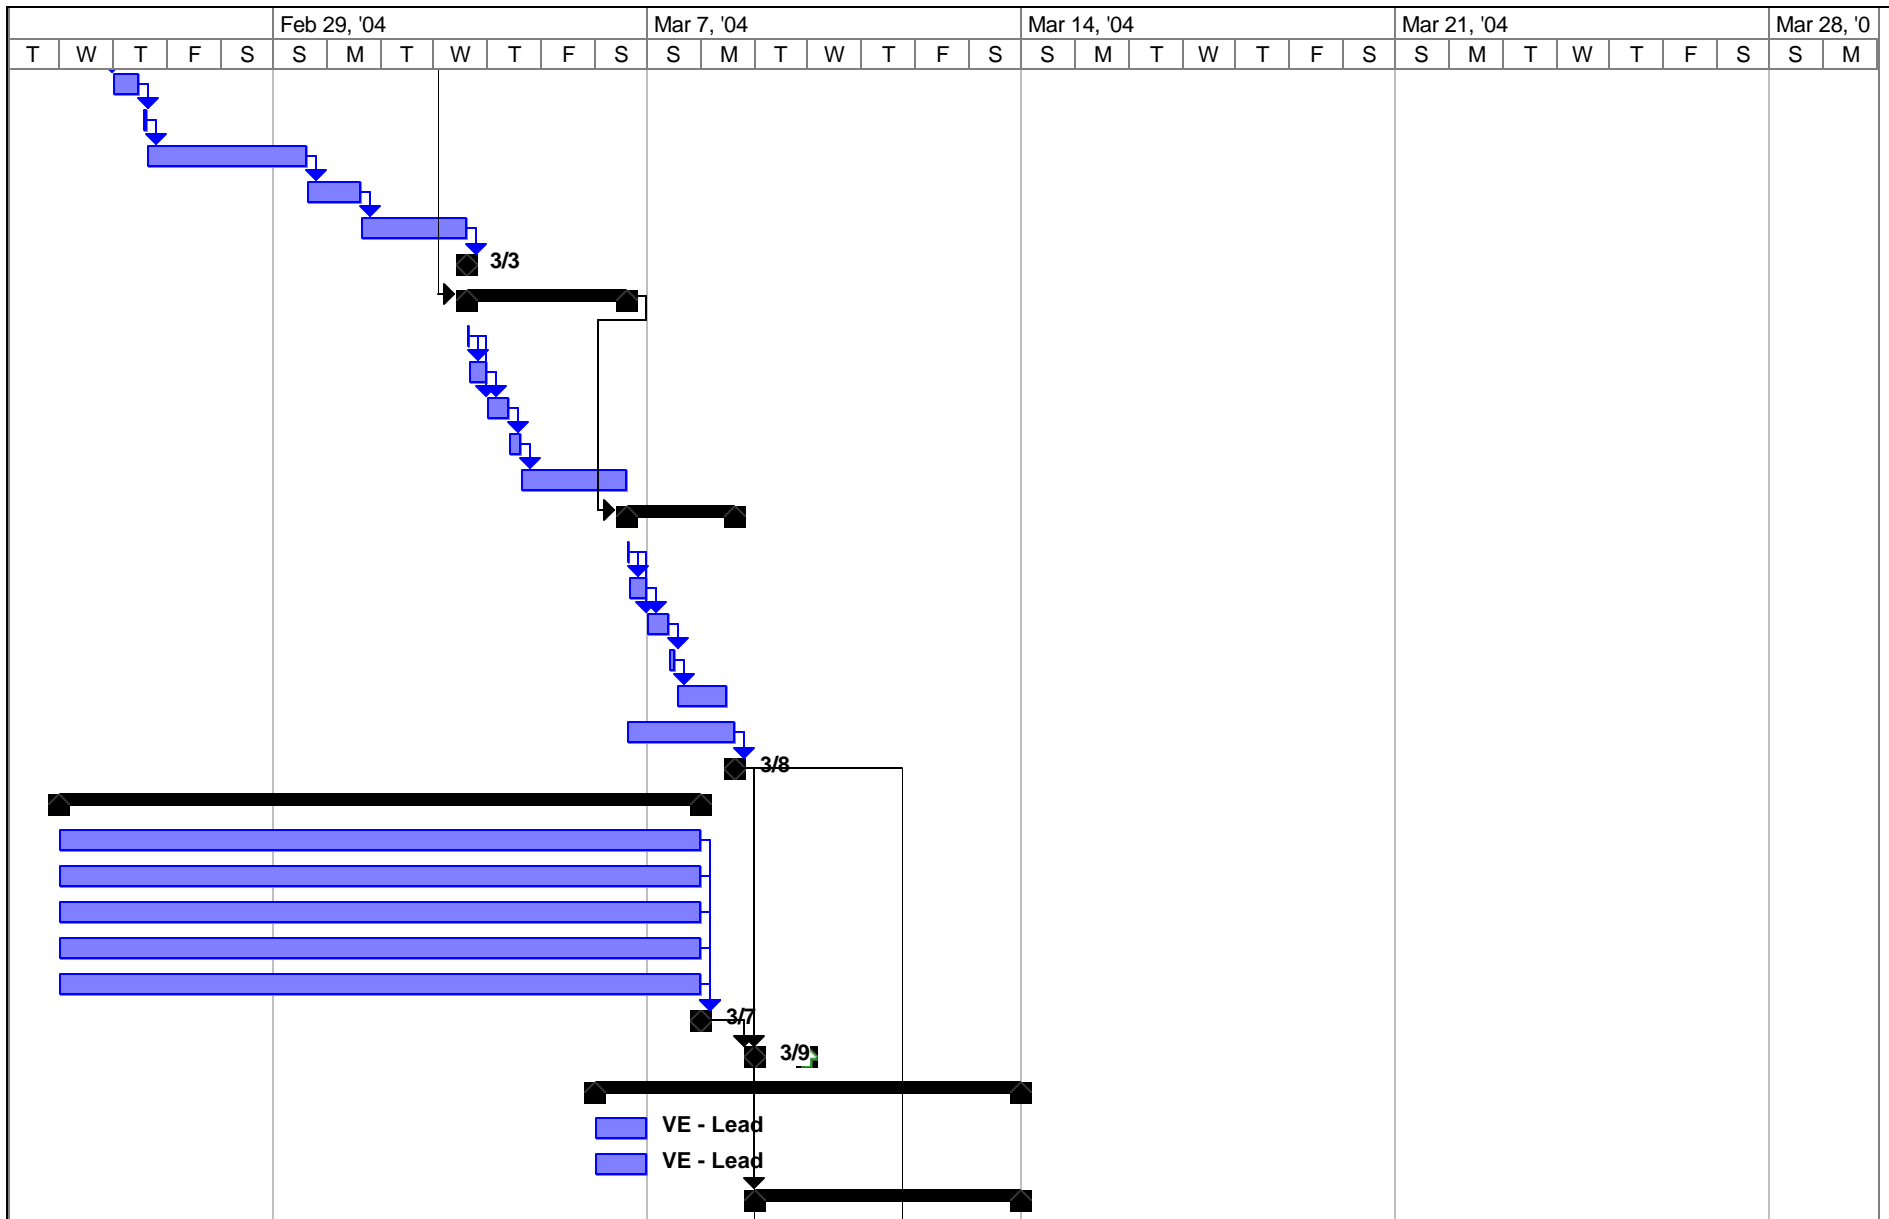

Project: PASAT Project Plan_v3
Date: Wed 6/16/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

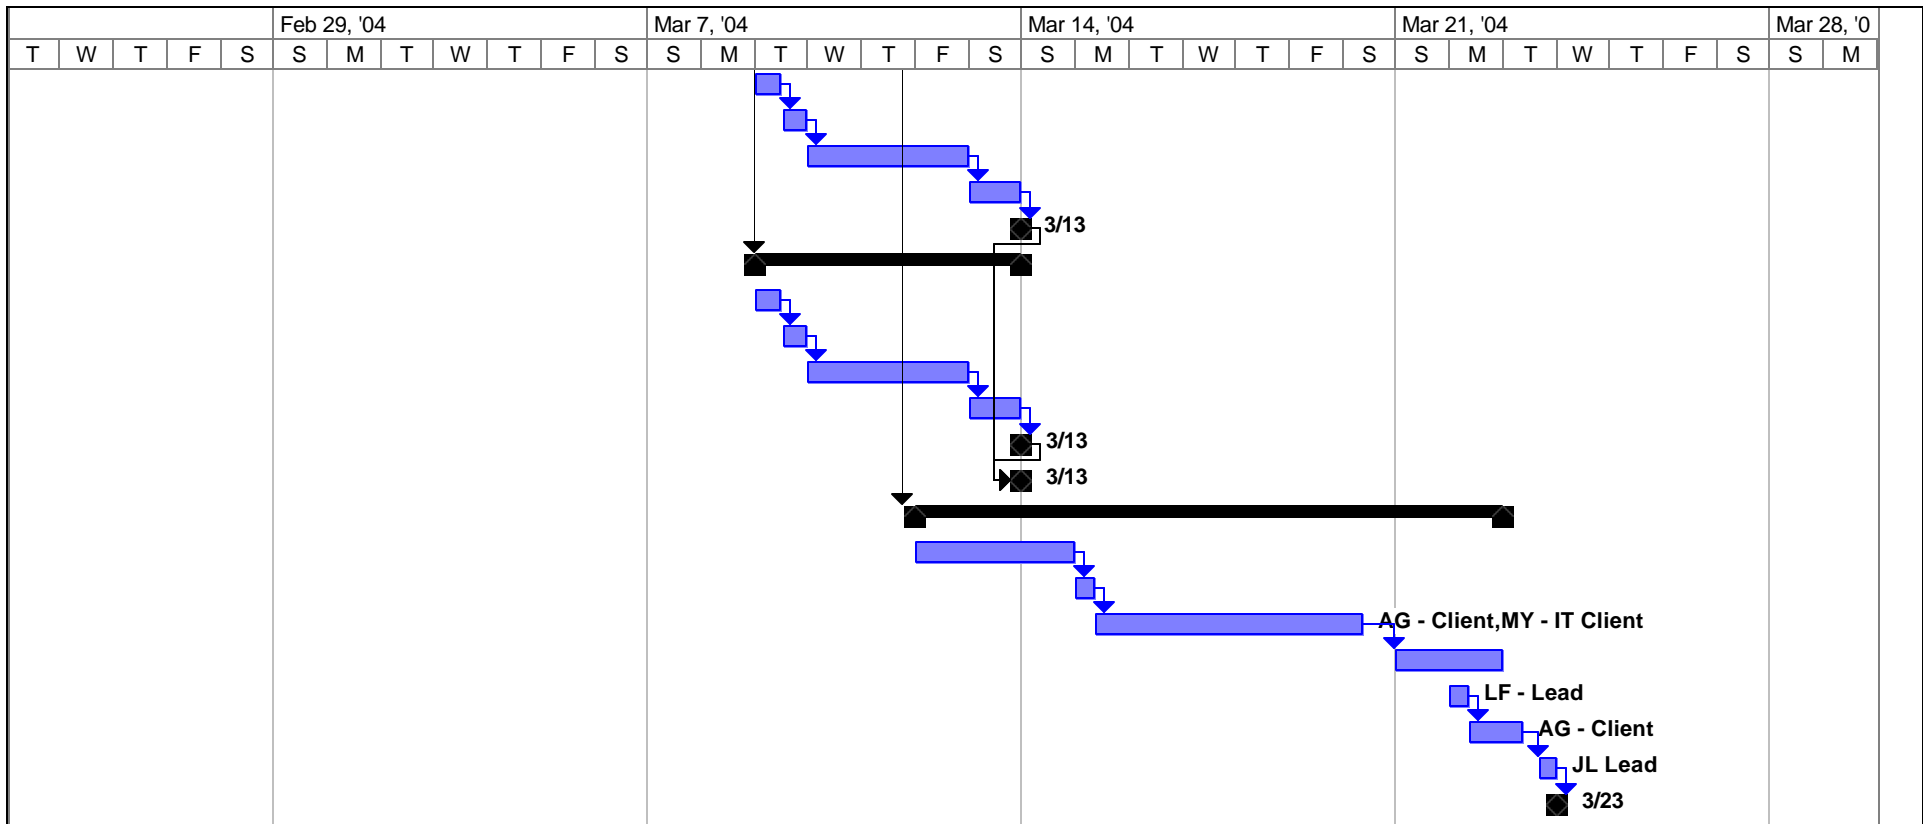

Project: PASAT Project Plan_v3
 Date: Wed 6/16/04

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
